



e-COMPANDIUM OF COMPLETED WORKS (2021-22)

APRIL, 2022

**HIGHER EDUCATION DEPARTMENT
GOVERNMENT OF JAMMU AND KASHMIR**

ABSTRACT OF COMPLETED PROJECTS UNDER VARIOUS SECTORS

S. No	Sector	No. of Projects	Completion Cost (In crore)	Outcome
1	Capex Budget	75	170.39	72,358 beneficiary students covered
2	PMDP	03	20.30	504 beneficiary students covered
3	RUSA	15	5.59	1910 beneficiary students covered
4	Languishing	18	61.61	
5	Local Fund	01	48.29	3000 beneficiary students covered
	Total	112	306.18	

S. No	Name of the Work/Project	Location	District	Executing Agency	Date of Start (Month/year)	AA Cost	Total Cost of Completion	Date of Completion (month/year)	No. of beneficiaries
Capex Budget									
1	Construction of College Building GDC Bani	GDC Bani	Kathua	JKPCC	2016	876.33	876.33	March,2022	500
2	Construction of College Building GDC Khilotran Doda	Khilotran Doda	Doda	JKPCC	2016	1335.5	1335.5	March,2022	880
3	Construction of College Building GDC SarhBagga Mahore	Bagga, village Sarh, Tehsil Mahore.	Reasi	JKPCC	Mar-17	441.20	430.10	Mar-22	208
4	Construction of College Building Banihal (Academic Block)	Bankoot	Ramban	JKPCC	2014	1886.90	1166.80	2021-22	450
5	Construction of 12 class room with allied infrastructure at GCW Udhampur	GCW Udhampur	Udhampur	R&B	2017	677.42	577.97	March, 2022	3000
6	Construction of Academic Block at GCW Anantnag	GCW Anantnag	Anantnag	J&K Housing Board	2017-18	616.00	616.00	2021-22	4913
7	Construction of Adm. Block AAM Degree College Bemina	GDC Bemina	Srinagar	PWD	2017	245.09	127.17	Mar-22	3450
8	Construction of Admission Block GDC Uttresoo	GDC Uttresoo	Anantnag	SICOP	2019	39.00	37.93	Mar-22	1113
9	Finishing of Girls Common Room at GGM Science College, Jammu	GGM Science College Jammu	Jammu	R&B	Mar-21	45.54	26.00	Oct-21	3500
10	Construction of Library Block at GCW	GCW	Anantnag	J&K	2017-18	249.00	249.00	2021-22	4913

S. No	Name of the Work/Project	Location	District	Executing Agency	Date of Start (Month/year)	AA Cost	Total Cost of Completion	Date of Completion (month/ year)	No. of beneficiaries
	Anantnag	Anantnag		Housing Board					
11	Construction of IT Block GDC Uttresoo	GDC Uttresoo	Anantnag	SICOP	2019	39.43	39.00	Mar-22	1113
12	Construction of Science Block at SP Collge srinagae	SP College	Srinagar	R&B	2017-18	481.74	481.74	2021-22	3109
13	Construction of Science Block(Phase 1) Women College Baramulla)	GCW Baramulla	Bara mulla	R&B Baramulla	14-12-2019	475.43	415.99	28.12.2021	2800
14	Construction of Auditorium Building Amar singh College Srinagar	Amar Singh College	Srinagar	JK Housing Board	2013-14	1280.00	1280.00	2021-22	4808
15	Construction Of Auditorium building Boys College Pulwama	GDC Pulwama	Pulwama	R &B	2014-15	612.09	612.09	2021-22	3594
16	Construction of Auditorium Building GDC Shopian	GDC shopian	Shopian	R & B	2016-17	658.11	658.11	2021-22	5081
17	Construction of Auditorium at GDC Sumbal	GDC Sumbal	Bandipora	J&K Housing Board	2020	993.07	955.97	2021-22	2521
18	Construction of 04 Additional Class rooms Block GCW Kathua	GC Women Kathua	Kathua	R&B	06/2019	240.00	138.87	Mar-22	320
19	Construction of 4 No. Science lab blocks GCW Udhampur	GCW Udhampur	Udhampur	R&B	2020	185.97	105.48	March, 2022	3000
20	Construction 08 room of Lecture Hall Block GCW Sopore	GDC Women Sopore	Baramulla	R&B	Oct-17	425.15	425.15	Mar-22	1065

S. No	Name of the Work/Project	Location	District	Executing Agency	Date of Start (Month/ year)	AA Cost	Total Cost of Completion	Date of Completion (month/ year)	No. of beneficiaries
21	Construction of 08 classroom block at GCW Anantnag	GCW Anantnag	Anantnag	SICOP	2015-16	528.00	528.00	2021-22	4913
22	Conversion of Old Hostel into class rooms GCW Parade	GCW Parade	Jammu	J&K PHC	2020	107.86	75.79	Mar-22	5700
23	Construction of Multipurpose Sports Hall including conference room/reading hall & Parking Shed at GDC Tangmarg	GDC Tangmarg	Baramulla	SICOP	Nov-21	150.00	148.99	Mar-22	1291
24	Construction of Multipurpose Hall GDC Pampore	Tulbagh, Pampore	Pulwama	SICOP	14/08/2020	66.06	66.06	August , 2021	1363
25	Construction of Prefabricated structure	Govt. Degree College for Women Kathua	Kathua	R&B	Feb-21	80.00	48.75	Mar-22	160
26	construction of Pre Fabricated hut GDC Hyderpora	GDC Hyderpora	Srinagar	R&B	31-10-2020	194.45	177.50	12-10-2021	203
27	Establishment of GDC Chenani (Const. of prefabricated structure)	GDC Chenani	Udhampur	SICOP	Oct-21	63.12	49.96	Feb.22	434
28	Construction of 03 Prefab huts for Class Rooms GDC Ramban	GDC Ramban	Ramban	R&B	2019-20	50.07	37.50	Dec .2021	730
29	Constuction of Wooden/Prefab facility and Residential quarter SP College	SP college	Srinagar	SICOP	Mar-21	35.78	35.78	Feb.22	3109
30	Construction of Pre-fabricated Hut	GDC Chadoora	Budgam	SICOP	13.03.2021	168.75	168.00	20.03.2022	171
31	Construction of Prefabricated	GDC Edidgah	Srinagar	R&B	Feb-20	40.56	40.56	Mar-22	151

S. No	Name of the Work/Project	Location	District	Executing Agency	Date of Start (Month/ year)	AA Cost	Total Cost of Completion	Date of Completion (month/ year)	No. of beneficiaries
	structure GDC Eidgah								
32	Construction of Prefabricated structure GDC Vailoo Larnoo	GDC Vailoo Larnoo	Anantnag	R&B	Nov-21	101.18	101.18	Mar-22	347
33	Construction of Prefabricated structure foe skill/research lab and PG block on first floor SPMR College Jammu	SPMR College Jammu	Jammu	SICOP	2021	88.00	87.74	Jan.2022	2770
34	Const. of Pre Fabricated Structure for 03 sill Development Centres at GDC Tangmarg	GDC Tangmarg	Baramulla	SICOP	May-21	51.00	49.16	Oct-21	1291
35	Pre-fabricated Structure for labs GDC Jourian	GDC Jourian	Jammu	R&B	2020	53.00	53.00	20.03.2022	314
36	Construction of Pre Fab Huts(4No.s) GDC Pampore	Tulbagh, Pampore	Pulwama	SICOP	19/09/2020	81.15	81.15	August, 2021	1363
37	Pre-fab structure of the college	Bhagwati Nagar	Jammu	R&B	.01.08.2020	114.97	94.92	..30.10.2021	278
38	Construction of Seprate tiolet Block GDC Uttresoo	GDC Uttresoo	Anantnag	SICOP	2019	37.57	35.91	Mar-22	1113
39	Construction of Toilet blocks GDC Kathua	GDC (Boys) Kathua	Kathua	JKPCC	Oct-17	71.60	71.60	Mar-22	4500
40	Construction of Toilet Block, Boundary wall, pre fabricated class rooms GDC Marh	GDC, Marh	Jammu	R&B	10-11-2020	124.31	93.55	30-10-2021	625
41	Construction of Canteen Block at GDC Nowshera	GDC Nowshera	Rajouri	R&B	Mar-21	35.60	32.29	Mar-22	1161

S. No	Name of the Work/Project	Location	District	Executing Agency	Date of Start (Month/ year)	AA Cost	Total Cost of Completion	Date of Completion (month/ year)	No. of beneficiaries
42	Construction of Virtual Lab GDC Pampore	Tulbagh, Pampore	Pulwama	SICOP	29-10-2020	80.00	65.00	March, 2022	1363
43	Setting of Chemistry Lab GDC Pampore	Tulbagh, Pampore	Pulwama	GEM	15-10-2021	20.00	20.00	March, 2022	1363
44	Browsing Centre GDC Basholi	GDC Basholi	Kathua	non const	Feb.2021	58.00	37.13	Dec-21	600
45	Automation of Library /laboratory at GDC Poonch	GDC Poonch	Poonch	R&B	Mar-21	30.00	29.99	Mar-22	1319
46	Development of Browsing Centre at GDC Women Anantnag	GCW Anantnag	Anantnag	non-const	2022	10.00	7.75	Mar-22	4913
47	Development of Browsing centre, with 60 KV Genset, hot & cold AC at GDC, Jourian)	GDC Jourian	Jammu	non Const	2021	18.00	12.67	Feb. 2022	314
48	Skill Centre at GDC Marh	GDC Marh	Jammu	R&B	04-02-2022	10.00	9.99	10-03-2022	625
49	Construction of Bore Well for under ground water	GDC Bani	Kathua	Jal Shakti PHE(M)	Mar-22	15.00	14.10	Mar-22	500
50	Const. of Chain Link Fencing of Additional Land at GDC Ramban	GDC Ramban	Ranmban	R&B	2019-20	53.90	53.90	Dec .2021	730
51	Construction of Chainlink fencing	GDC Chadoora	Budgam	SICOP	24.02.2021	83.61	83.61	20.03.2022	171
52	renovation of make shift accommodation GDC Zainpora	GDC Zainpora	Shopian	R&B	Mar-20	15.00	12.18	Aug-21	354
53	Up gradation of College Buildings by way of damaged plaster, painting, vitrified tiling GDC Baramulla	GDC Baramulla	Baramulla	SICOP	2020-21	69.16	33.00	Dec.2021	4130
54	Imprvment/Upgradation including	GCW Gandhi	Jammu	R&B	Dec-19	121.00	120.64	Oct-21	6000

S. No	Name of the Work/Project	Location	District	Executing Agency	Date of Start (Month/year)	AA Cost	Total Cost of Completion	Date of Completion (month/ year)	No. of beneficiaries
	water proofing of seven blocks GCW Gandhi Nagar, Jammu	Nagar							
55	Repair and Renovation of Principal Office GCW Gandhi Nagar, Jammu	GCW Gandhi Nagar	Jammu	R&B	Mar-21	20.70	11.64	Aug-21	300
56	Up-gradation and modernisation of college Buildings(Adm block,Browsing centre)at GCW Baramulla)	GCW Baramulla	Bara mulla	R&B Baramulla	01-06-2021	30.00	25.02	28.12.2021	2800
57	Up-gradation of Auditorium at GDC Women Anantnag	GCW Anantnag	Anantnag	GeM/R&B Division Khanabal	2021	20.00	10.82	Mar-22	4913
58	Repair/ reno. of BCA room Govt. Degree College Poonch	GDC Poonch	Poonch	R&B	Mar-21	11.96	11.61	Mar-22	50
59	Repair/ reno. of Washroom in GDC Poonch	GDC Poonch	Poonch	R&B	Mar-21	12.70	12.70	Mar-22	50
60	Raising / Repair of mesh wire fencing around GDC Baramulla	GDC Baramulla	Baramulla	SICOP	2020-21	66.71	66.71	Feb.2022	4130
61	Repairing of Guest House at GGM Science College, Jammu	GGM Science College Jammu	Jammu	R&B	Apr-21	33.22	20.70	Jul-21	3500
62	Const. Of Paths by way of cement concrete bed with precast cement concrete tiles along road and Botanical garden at SP College	SP college	Srinagar	SICOP	Mar-21	10.42	10.42	Feb.22	3109
63	Construction of Boundary wall with drain Sp College	SP college	Srinagar	SICOP	Mar-21	44.53	44.53	Feb.22	3109

S. No	Name of the Work/Project	Location	District	Executing Agency	Date of Start (Month/ year)	AA Cost	Total Cost of Completion	Date of Completion (month/ year)	No. of beneficiaries
64	Construction of Bus Shed and store room at GDC Baramulla	GDC Baramulla	Baramulla	SICOP	2020-21	18.85	15.55	Jan.2022	4130
65	Construction of Parking Shed for Students & Staff at GGM Science College, Jammu	GGM Science College Jammu	Jammu	R&B	May-21	81.67	50.00	Sep-21	3500
66	Construction of Car Parking with steel roof truss	SP college	Srinagar	SICOP	Mar-21	21.91	21.91	Feb.22	3109
67	Construction of Car ParkingGDC Pampore	Tulbagh, Pampore	Pulwama	SICOP	25-09-2020	34.85	34.85	August, 2021	1363
68	Platform GDC Marh	GDC Marh	Jammu	R&B	20-11-2021	11.54	6.67	15-02-2022	625
69	Aluminium partition at GDC Marh	GDC Marh	Jammu	R&B	30-11-2021	5.52	3.29	20-01-2022	625
70	63 KVA sub station GDC Marh	GDC Marh	Jammu	R&B	10-01-2022	7.41	7.15	05-03-2022	625
71	Ground Leveling GDC Ramban	GDC Ramban	Ramban	R&B	2019-20	21.84	16.63	Dec .2021	730
72	Construction of nursing and medical institute IUST	Awantipora	Pulwama	Engg. Wing of University	2014-15	707.61	707.61	2021-22	-
73	Construction of Central Library at BGSBU Rajouri	Rajouri	Rajouri	Engg. Wing of University	2016	1091.70	1091.70	2021-22	-
74	Construction of Botany and Zoology block at BGSBU Rajouri	Rajouri	Rajouri	Engg. Wing of University	2016-17	687.00	687.00	2021-22	-
75	School of Paramedical College South Campus Kashmir University	Kashmir University	Srinagar	Engg. Wing of University	2016-17	1050.00	1050.00	2021-22	-


S. No	Name of the Work/Project	Location	District	Executing Agency	Date of Start (Month/year)	AA Cost	Total Cost of Completion	Date of Completion (month/year)	No. of beneficiaries
	Total					18619.81	17039.06		
	PMDP								
1	Construction of Girls Hostel at GDC Paloura	GDC Paloura	Jammu	Housing Board	Jul-17	1250.00	1125.00	Oct-21	300
2	Construction of Girls Hostel at GDC Badherwah	GDC Badherwah	Doda	PHC	Nov-18	500.00	450.00	Dec-21	80
3	Construction of Girls Hostel GDC Rajouri	GDC Rajouri	Rajouri	Housing Board	15.05.2018	500.00	455.86	Mar-22	124
	Total					2250	2030.86		504
RUSA-Centrally Sponsored scheme									
1	Construction of Toilet Block for Girls GDC Poonch	GDC Poonch	Poonch	PWD (R&B)	Mar-21	12.31	12.31	Mar-22	980
2	Upgradation of Canteen/ Cafeteria GDC Poonch	GDC Poonch	Poonch	PWD (R&B)	Mar-21	3.58	3.58	Jan-22	1913
3	Repair / renovation / Upgradation of Existing Auditorium GDC Poonch	GDC Poonch	Poonch	PWD (R&B)	Mar-21	9.50	9.50	Jan-22	1913
4	Common Room Facility for Students GDC Poonch	GDC Poonch	Poonch	PWD(R&B)	Mar-21	43.28	43.28	Mar-22	1913
5	Repair / renovation Upgradation of Class Rooms GDC Poonch	GDC Poonch	Poonch	PWD(R&B)	Mar-21	7.98	7.98	Jan-22	100
6	Construction of Canteen Block at GDC Sunder bani	GDC Sunderbani	Rajouri	PWD (R&B)	Dec-20	23.25	23.25	Mar-22	913
7	Construction of Toilet Block at GDC	GDC	Rajouri	PWD	Dec-20	44.65	44.65	Mar-22	913

S. No	Name of the Work/Project	Location	District	Executing Agency	Date of Start (Month/year)	AA Cost	Total Cost of Completion	Date of Completion (month/ year)	No. of beneficiaries
	Sunder bani	sunderbani		(R&B)					
8	Common Room Facility for Students GDC Rajouri	GDC Rajouri	Rajouri	PWD (R&B)	Dec-20	79.60	45.00	Jan-22	2500
9	Repair Renovation / Adition & altration of Staff Room & office GCE Udhampur	GCW Udhampur	Udhampur	PWD (R&B)	Jun-20	59.50	44.00	Oct-21	100
10	Construction of Girls Common Room	GCW Udhampur	Udhampur	PWD (R&B)	Mar-21	99.00	36	Mar-22	3000
11	Construction of Toilet Block GDC Larnoo	GDC Larnoo	Anantnag	PWD (R&B)	Nov-20	43.88	41.40	Mar-22	
12	Construction of Toilet Block Male/ Female GDC Kupwara	GDC Kupwara	Kupwara	JKPCC	Jun-18	44.65	44.65	Jan-22	540
13	Construction of Canteen Block at GDC Kupwara	GDC Kupwara	Kupwara	JKPCC	Jun-18	23.25	23.25	Jan-22	540
14	Construction of Additional Class Room GDc Udhampur	Udhampur	Udhampur	PWD(R&B)	Jul-19	99.5	60.25	Jul-21	700
15	Construction of Administrative Block of Jammu University	Jammu university	Jammu	PWD(R&B)	2019-20	120.00	120.00	Mar-22	130
	Total					713.93	559.1		1910
Local Fund									
01	Construction of canteen complex in the GCW Udhampur	GCW Udhampur	Udhampur		2019	48.29	48.29	2021	3000

Details of completed Languishing Projects.

S. No.	Name of the Project	LUP Code	Name of the Institute	Approved cost by JKIDFC (in crores)	Payment Released by JKIDFC so far	Date of initiation	Year of Completion
1	Kathua Campus Academic Block	LUP1688	Jammu University	2.50500	2.06114	2019	2021
2	Kathua Campus Boys Hostel	LUP1689	Jammu University	1.98530	1.69412	2019	2021
3	Kathua Campus Girls Hostel	LUP1690	Jammu University	2.44820	1.43492	2019	2021
4	Ramnagar Campus Academic Block	LUP1685	Jammu University	0.94400	0.43173	2019	2021
5	Ramnagar Campus Boys Hostel	LUP1686	Jammu University	2.71840	0.75226	2019	2021
6	Ramnagar Campus Girls Hostel	LUP1687	Jammu University	2.15120	0.75588	2019	2021
7	Reasi Campus Academic Block	LIP1695	Jammu University	1.33880	1.13578	2019	2021
8	Reasi Campus Girls Hostel	LUP1697	Jammu University	3.10680	0.00000	2019	2021
9	Boys Hostel, Reasi Campus	LUP1696	Jammu University	3.19842	1.18426	2019	2021
10	Construction of Girls Hostel Main Campus	LUP2547	Kashmir University	1.39230	0.00000	2019	2021
11	Construction of New Administrative Block	LUP2548	Kashmir University	7.68000	0.00000	2019	2021
12	Laboratory Block (PEB) Main Campus	LUP2549	Kashmir University	5.02000	1.36449	2019	2021
13	Islamic University Library Block	LUP2637	IUST, Awantipora	8.0000	4.92711	2019	2021
14	Islamic University-	LUP2640	IUST, Awantipora	2.0000	0.58833	2019	2021

	Residential Quarters						
15	Islamic University- Mantaqi School Awantipora	LUP2638	IUST, Awantipora	4.4144	3.38224	2019	2021
16	Islamic University- Nursing Hostel Charar-i	LUP2639	IUST, Awantipora	7.8600	6.36916	2019	2021
17	Constrution of Prefabricated 04 classrooms and 04 labs	LUP1682	GDC Bishnah	1.2867	0.91507	2019	2021
18	Academic Block	LUP1681	GDC Akhnoor	3.5629	2.03759	2019	2021
G. Total				61.61242	29.03408		

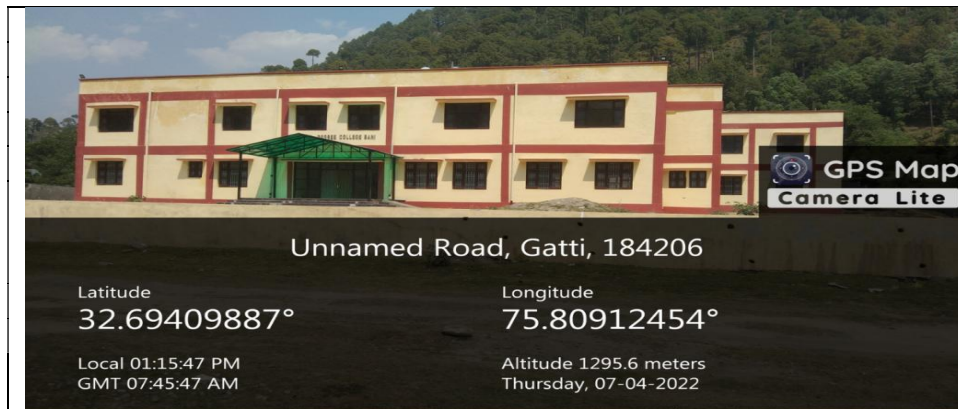

Name of the work with Location	College Building / GDC Bani
Department/Organization	GDC Bani
Executive Agency	JKPCC LTD, Unit Kathua
Block/District	Bani/ Kathua
AA Cost (Rs. in Lakhs)	876.33
Total Cost of Completion/Expenditure incurred ending 3/2022	876.33
Year of Start	2016
Year of Completion	2022
No. of beneficiaries	500 Students



Name of the work with Location	Construction of College Building at GDC Khilotran
Department/Organization	Higher Education/GDC Khilotran
Executive Agency	JKPCC LTD, Unit Kathua
Block/District	Changa/Doda
AA Cost (Rs. in Lakhs)	1335.50
Total Cost of Completion/Expenditure incurred ending 3/2022	1335.50
Year of Start	2016
Year of Completion	2022
No. of beneficiaries	8880



Name of the work with Location	Construction of College Building GDC SarhBagga Mahore
Department/Organization	Higher Education Department
Executive Agency	JKPCC
Block/District	Mahore/Reasi
AA Cost (Rs. In lakhs)	441,20
Total Cost of Completion/Expenditure incurred ending 3/2022	431.10
Date of Start (Month/Year)	March-2017
Date of Completion (Month/Year)	March 2022
No. of beneficiaries	208



Name of the work with Location	Construction of Govt. Degree College Banihal at Bankoot
Department/Organization	Higher Education Department
Executive Agency	JKPCC Ltd.
Block/District	Banihal/Ramban
AA Cost (Rs. In lakhs)	1886.90 Lacs
Total Cost of Completion/Expenditure incurred ending 3/2022	1166.80 Lacs
Date of Start (Month/Year)	April-2014
Date of Completion (Month/Year)	Only Academic Block of the College has been made functional w.e.f 04-04-2022
No. of beneficiaries	450



Name of the Work with Location	Construction of 12 class room with allied infrastructure at GCW Udhampur
Department/Organization	Higher Education/GCW udhampur
Executive Agency	R&B
Block/District	Udhampur
AA Cost (Rs. In lakhs)	677.42
Total Cost of Completion/Expenditure incurred ending 3/2022	577.97
Date of Start (Month/Year)	2017
No. of Beneficiaries	3000



Name of the Work with Location	Construction of Academic Block GCW Anantnag
Department/Organization	Higher Education
Executive Agency	R&B
Block/District	Anantnag
AA Cost (Rs. In lakhs)	616.00
Total Cost of Completion/Expenditure incurred ending 3/2022	616.00
Date of Start (Month/Year)	2017-18
No. of Beneficiaries	4913



Name of the Work with Location	Construction of Administrative Block AAAM Degree College Bemina Sgr.
Department/Organization	Bemina
Executive Agency	PW(R&B) Department , Executive Engineer , CD II Sgr.
Block/District	Srinagar
AA Cost (Rs. In lakhs)	245.09
Total Cost of Completion/Expenditure incurred ending 3/2022	127.17
Date of Start (Month/Year)	2017
No. of Beneficiaries	3450



Name of the Work with Location	Construction of Admission Block
Department/Organization	Higher Education (GDC Uttresoo)
Executive Agency	SICOP
Block/District	Shangus/Anantnag
AA Cost (Rs. In lakhs)	Rs.39.00 lacs
Total Cost of Completion/Expenditure incurred ending 3/2022	Rs.37.93 lacs
Date of Start (Month/Year)	2019
No. of Beneficiaries	1113



Name of the work with Location	Finishing of Girls Common Room at GGM Science College, Jammu
Department / Organization	Higher Education Department
Executive Agency	PWD
Block / District	Jammu
AA Cost (Rs. in lakhs)	Rs. 46.54 Lacs
Total Cost of Completion / Expenditure incurred ending 3/2022	Rs. 26.00 Lacs
Date of Start (Month / Year)	March / 2021
Date of Completion (Month / Year)	Oct / 2021
No. of beneficiaries	3500



Name of the work with Location	Construction of Library Block at GCW Anantnag
Department / Organization	Higher Education Department
Executive Agency	J&K Housing Board
Block / District	Anantnag
AA Cost (Rs. in lakhs)	Rs. 249.00 lacs
Total Cost of Completion / Expenditure incurred ending 3/2022	Rs. 249.00 Lacs
Date of Start (Month / Year)	2017-18
Date of Completion (Month / Year)	2021-22
No. of beneficiaries	4913




Name of the Work with Location	Construction of IT Block
Department/Organization	Higher Education(GDC Uttresoo)
Executive Agency	SICOP
Block/District	Shangus/Anantnag
AA Cost (Rs. In lakhs)	Rs.39.43 lacs
Total Cost of Completion/Expenditure incurred ending 3/2022	Rs.39.00 lacs
Date of Start (Month/Year)	2019
No. of Beneficiaries	1113



SCHOOLE OF SCIENCES Three Storeys + Stilt Parking

Name of the Project	Science Block Sp College Sgr.
Department/Organization	Higher Education Department
Executing Agency	R&B
Block/District	Srinagar
AA Cost (Rs. In lakhs)	481.74
Total Cost of Completion/Expenditure incurred ending 3/2022	481.74
Date of Start (Month/Year)	2017-18
No. of Beneficiaries	3109

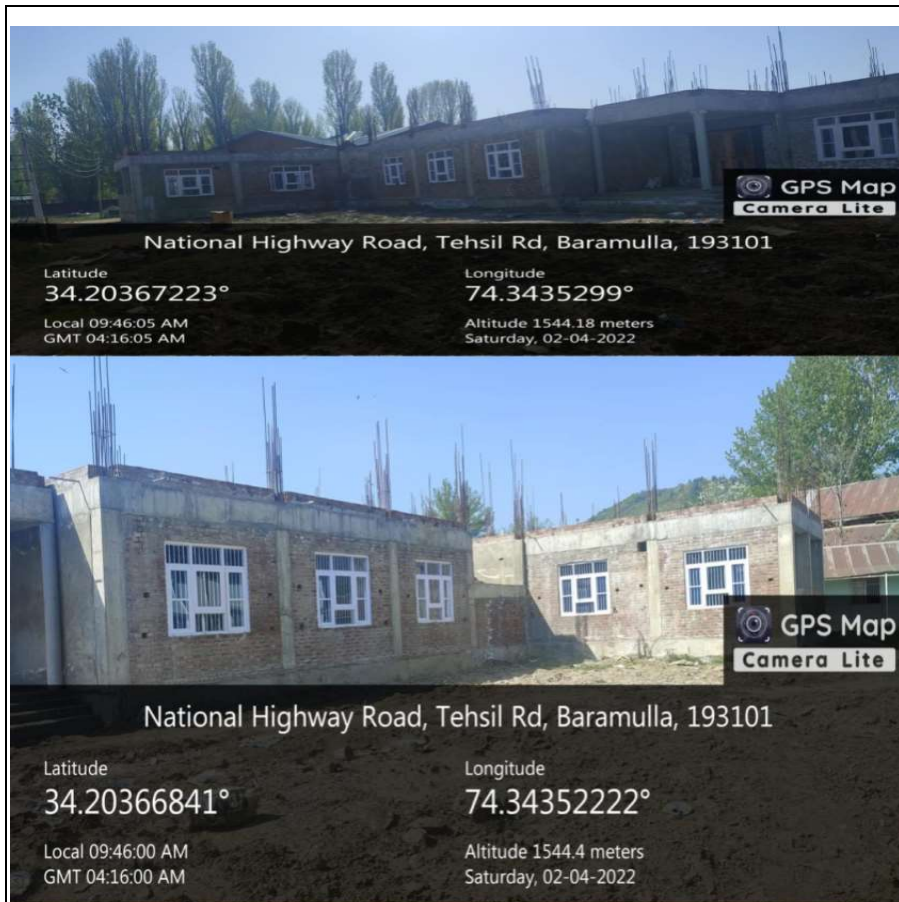

Name of the work with Location	Construction of Science Block(Phase 1) Women College Baramulla)
Department / Organization	Higher Education/GCW Baramulla
Executive Agency	R&B
Block / District	Baramulla
AA Cost (Rs. in lakhs)	475.43
Total Cost of Completion / Expenditure incurred ending 3/2022	415.99
Date of Start (Month / Year)	14.12.2019
Date of Completion (Month / Year)	28.12.2021
No. of beneficiaries	2800



Name of the Project	Auditorium building Amar Singh College Sgr..
Department / Organization	Higher Education
Executing Agency	JK Housing Board
Block/District	Srinagar
AA Cost (Rs. In lakhs)	1280.00
Total Cost of Completion/Expenditure incurred ending 3/2022	1280.00
Date of Start (Month/Year)	2013-14
No. of Beneficiaries	4808



Name of the Project	Construction of Auditorium Building GDC Pulwama
Department / Organization	Higher Education
Executing Agency	R & B
Block/District	Pulwama
AA Cost (Rs. In lakhs)	612.09
Total Cost of Completion/Expenditure incurred ending 3/2022	612.09
Date of Start (Month/Year)	2014-15
No. of Beneficiaries	3594




Name of the Project	Construction of Auditorium Building GDC Shopian
Department / Organization	Higher Education
Executing Agency	R & B
Block/District	Shopian
AA Cost (Rs. In lakhs)	658.11
Total Cost of Completion/Expenditure incurred ending 3/2022	658.11
Date of Start (Month/Year)	2016-17
No. of Beneficiaries	5081



Name of the Project	Auditorium building GDC Sumbal
Department / Organization	Higher Education
Executing Agency	J&K Housing Board
Block/District	Sumbal/Bandipora
AA Cost (Rs. In lakhs)	993.07
Total Cost of Completion/Expenditure incurred ending 3/2022	955.97
Date of Start (Month/Year)	2020
No. of Beneficiaries	2521



Name of the Work with locatio	Construction of 04 Additional Class rooms Block :
Department/Organization	Higher Education
Executive Agency	R&B, PWD
Block /District	Kathua/GCW Kathu
AA Cost (Rs. In lakhs)	240.00
Total cost of completion/Expenditure incurred ending 3/2022	138.87
Date of Start (Month/Year)	06/2019
Date of Completion (Month/Year)	03/2022
No. of beneficiaries	320

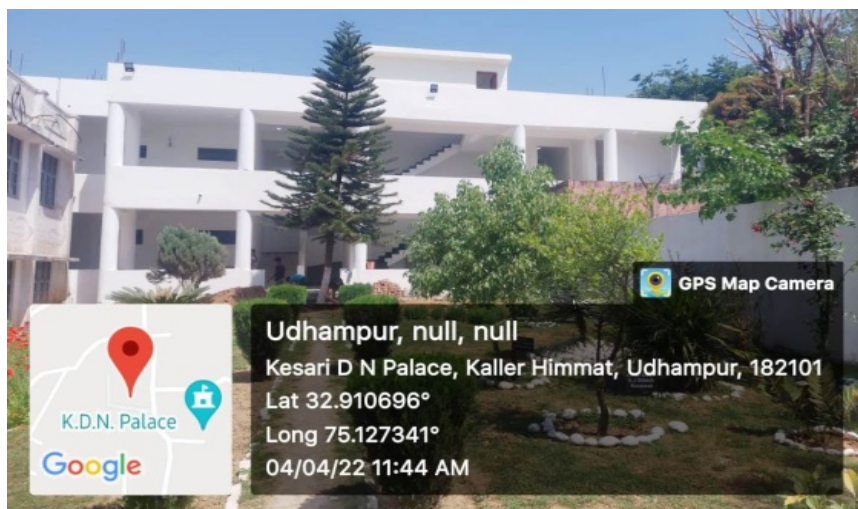

Name of the Work with Location	Construction of 4 No. Science lab blocks at GCW Udhampur
Department/Organization	Higher Education
Executive Agency	R&B
Block/District	Udhampur
AA Cost (Rs. In lakhs)	185.97
Total Cost of Completion/Expenditure incurred ending 3/2022	105.48
Date of Start (Month/Year)	2020
No. of Beneficiaries	3000



Name of the Work with location	8 Room Lecture Hall Block
Department/Organization	GDC Women Sopore
Executive Agency	R&B
Block /District	Baramulla
AA Cost (Rs. In lakhs)	425.15
Total cost of completion/Expenditure incurred ending 3/2022	425.15
Date of Start (Month/Year)	10/2017
Date of Completion (Month/Year)	03/2022
No. of beneficiaries	1065



Name of the Work with Location	Construction of 08 classroom black at GCW Anantnag
Department/Organization	Higher Education
Executive Agency	SICOP
Block/District	Anantnag
AA Cost (Rs. In lakhs)	528.00
Total Cost of Completion/Expenditure incurred ending 3/2022	528.00
Date of Start (Month/Year)	2015-16
No. of Beneficiaries	4913




Name of the work with location	Conversion of Old Hostel into class rooms
Department/Organization	Higher Education/GCW parade
Executive Agency	Police Housing Corporation
Block/District	Jammu/Jammu
AA Cost (Rs. In lakhs)	107.86
Total Cost of Completion/Expenditure incurred ending 03/2022	75.79
Date of Start (Month/Year)	2020
Date of Completion(Month/Year)	March-22
No. oBeneficiaries	5700



Name of the work with Location	Construction of Multipurpose Sports Hall including conference room/reading hall & Parking Shed
Department/organization	Higher Education/GDC Tangmarg
Executing Agency	SICOP
Block/District	Tangmarg/Baramulla
AA Cost (Rs. In Lakhs)	150.00
Total Cost of completion /expenditure incurred ending 3/2022	148.99
Date of Start (month/Year)	Nov-21
Date of Completion (month/Year)	March-21
No. Of beneficiaries	1291



Name of the Work with Location	Construction of Multipurpose Hall
Department/Organization	Higher Education Department/GDC Pampore
Executive Agency	SICOP
Block/District	Pulwama
AA Cost (Rs in Lacs)	66.06
Total cost of Completion/Expenditure incurred ending 3/2022	66.06
Date of Start (M/Y)	14/08/2020
Date of Completion	August-22
No of beneficiaries	1363

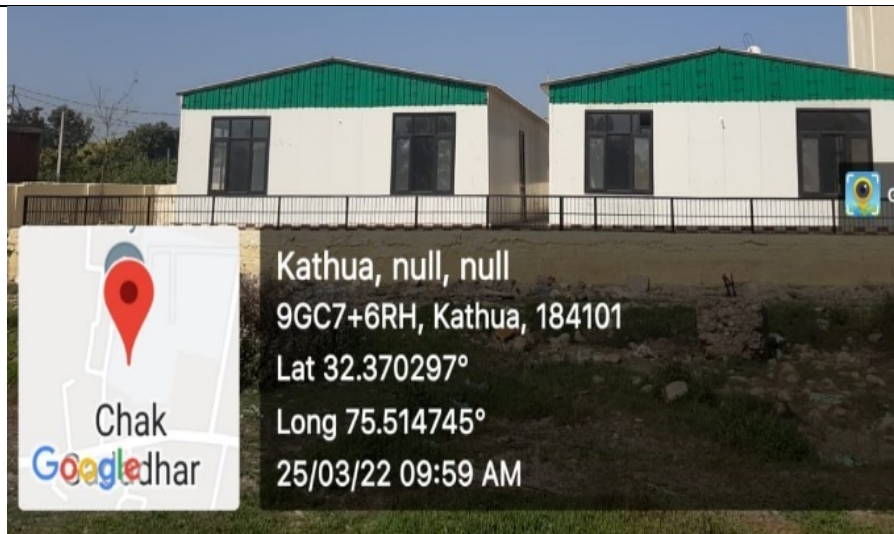

Name of the Work with location	Construction of Prefabricated Structure	
Department/Organisation	Higher Education	
Executive Agency	R&B, PWD	
Block /District	Kathua	
AA Cost (Rs. In lakhs)	80.00	
Total cost of completion/Expenditure incurred ending 3/2022	48.75	
Date of Start (Month/Year)	02/2021	
Date of Completion (Month/Year)	03/2022	
No. of beneficiaries	160	



Name of the work with Location	Const. of Prefab. Hut
Department/Organization	Higher Education (GDC hyderpora)
Executive Agency	PWD(R&B)
Block/District	Srinagar/Srinagar
AA Cost (Rs. In lakhs)	194.45
Total Cost of Completion/Expenditure incurred ending 3/2022	177.50
Date of Start (Month/Year)	31.10.2020
Date of Completion (Month/Year)	12.10.2021
No. of beneficiaries	203



Name of the work with Location	Construction of Pre Fabricated Structure
Department / Organization	Higher Education Department/GDC Chenani
Executive Agency	SICOP
Block / District	Chenani/Udhampur
AA Cost (Rs. in lakhs)	Rs. 63.12 Lacs
Total Cost of Completion / Expenditure incurred ending 3/2022	Rs. 49.96 Lacs
Date of Start (Month / Year)	Oct. / 2020
Date of Completion (Month / Year)	Feb. / 2022
No. of beneficiaries	434



Name of the work with Location:	03 Prefab huts for Class Rooms
Department/Organization	Higher Education Deptt. (GDC Ramban)
Executing Agency	PWD (R&B) Ramban
Block/District	Ramban
AA Cost in Lakhs	50.07 lacs
Total Expdt. Incurred ending 3/2022	37.50 lacs
Project Initiation Year	2019-20
Date of Completion MM/YY	Dec. 2021
No of beneficiaries	730



Name of the work with Location:	Construction of wooden/prefab facility and residential wuarter at SP college
Department/Organization	Higher Education
Executing Agency	SICOP
Block/District	Srinagar
AA Cost in Lakhs	35.78
Total Expdt. Incurred ending 3/2022	35.78
Project Initiation Year	March 2021
Date of Completion MM/YY	Feb. 22
No of beneficiaries	3109





Name of the work with Location	Construction of Pre-fabricated Hut
Department/organization	Higher Education/GDC Chadoora
Executing Agency	SICOP
Block/District	Chadoora
AA Cost (Rs. In Lakhs)	168.75
Total Cost of completion /expenditure incurred ending 3/2022	168.00
Date of Start (month/Year)	13.03.2021
Date of Completion (month/Year)	20.03.2022
No. Of beneficiaries	171




Name of the work with location	Prefabricated huts (02 no) for GDC Idgah, Eidgah Saidpora Srinagar
Department /organization	Higher Education
Executing agency	JK SICOP SRINAGAR
Block district	EIDGAH
AA cost (Rs in lakhs)	40.56
Total cost of completion /expenditure incurred ending 3/2022	40.56
Date of start (month /year)	02/2020
Date of completion (month /year)	29/03/2022
No of beneficiaries	151



Name of the work with location	Construction of pre fab- huts (CAPEX)
Department /organization	Higher Education Department GDC Vailoo Larnoo
Executing agency	PWD (R&B) Division Vailoo
Block district	Larnoo/Anantnag
AA cost (Rs in lakhs)	101.18
Total cost of completion /expenditure incurred ending 3/2022	101.18
Date of start (month /year)	11/2020
Date of completion (month /year)	March-2022
No of beneficiaries	347

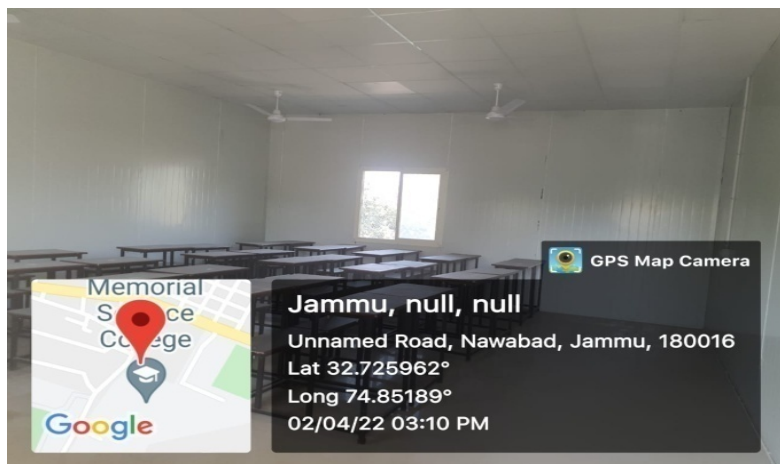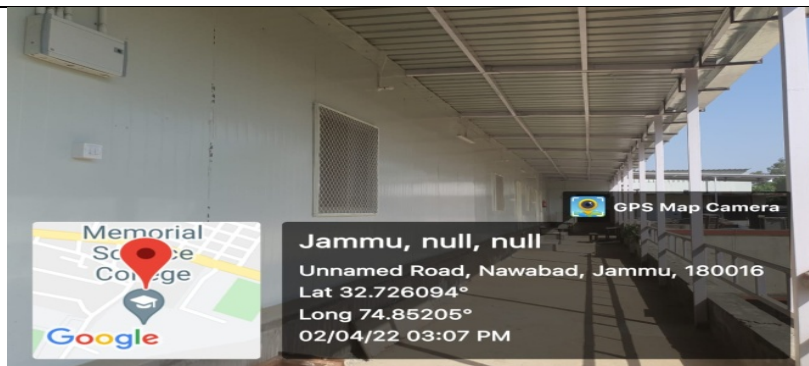

Name of the work with location	Construction of Prefabricated structure for skill/research lab and PG block on first floor.
Department /organization	Higher Education Department /SPMR College, Jammu
Executing agency	SICOP
Block district	Jammu
AA cost (Rs in lakhs)	88.00
Total cost of completion /expenditure incurred ending 3/2022	87.74
Date of start (month /year)	2021
Date of completion (month /year)	March-2022
No of beneficiaries	2770

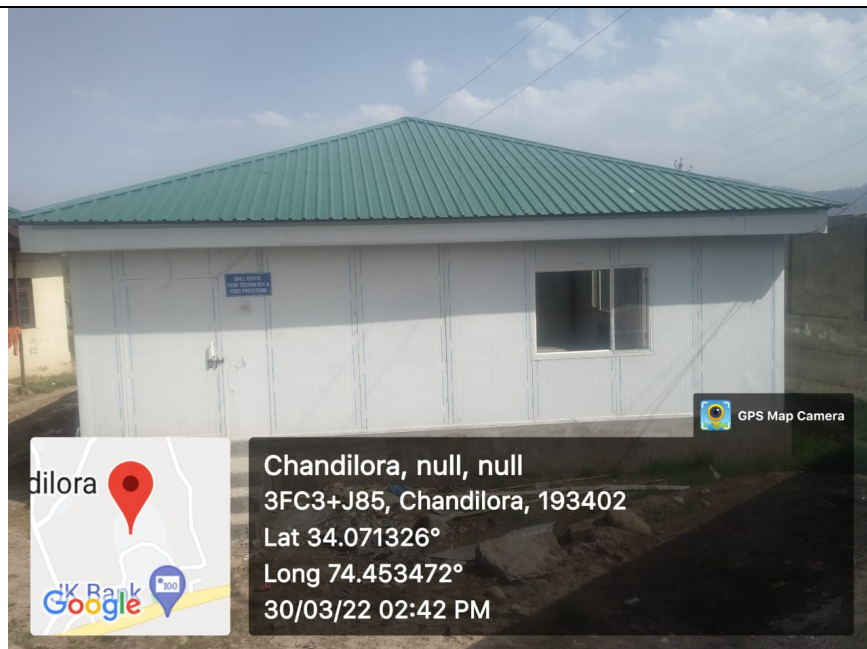

Name of the work with Location	Const. of Pre Fabricated Structure for 03 sill Development Centers at GDC Tangmarg
Department/organization	Higher Education/GDC Tangmarg
Executing Agency	SICOP
Block/District	Tangmarg/Baramulla
AA Cost (Rs. In Lakhs)	51.00
Total Cost of completion /expenditure incurred ending 3/2022	49.16
Date of Start (month/Year)	May-21
Date of Completion (month/Year)	October-21
No. Of beneficiaries	1291



Name of the Work with Location	Establishment of GDC Jourian (Pre-fabricated Structure for labs)
Department/Organization	Govt. Degree College Jourian
Executing Agency	PWD (R&B)
Block/District	BhalwalBrahmana/Jammu
Estimated Cost (Rs.in Lakhs)	53.00.lakhs
Total Expd. incurred ending 03/2022 (Rs. in Lakhs)	53.00.lakhs
Project initiation year	2020
Date of Completion	20.03.2022
No. of beneficiaries	314



Sr.NO.	62
Name of the Work with Location	Construction of Pre Fab Huts(4No.s)
Department/Organization	Higher Education Department
Executive Agency	SICOP
Block/District	Pulwama
AA Cost (Rs in Lacs)	81.15
Total cost of Completion/Expenditure incurred ending 3/2022	81.15
Date of Start (M/Y)	19/09/2020
Date of Completion	July, 2022
No of beneficiaries	1363

OFFICE OF THE PRINCIPAL,
GOVT. COLLEGE FOR WOMEN,
BHAGWATI NAGAR, JAMMU- 180001 (UT OF J&K) – INDIA





PROF. MINNIE SHARMA
PRINCIPAL
NO:-GCWBN/COLL/2022/52

Mobile No : 09419188878(O)
E-Mail: gcwbn19@gmail.com
DATED :15/03/2022

	<p>Sr. no</p> <p>Name of the work with location</p> <p>Department</p> <p>Executing agency</p> <p>Block / District</p> <p>AA cost</p>	<p>01</p> <p>Pre –fab structure of the college at Gole Gujral Bhagwati nagar Jammu</p> <p>Higher Education</p> <p>PWD (R&B)</p> <p>Marh/ Jammu</p> <p>114.97 lac</p>
--	--	--

	<p>Total cost of the completion /Expenditure incurred ending 3/2022</p> <p>Date of start</p> <p>Date of completion</p> <p>No of beneficiaries</p>	<p>94.92 lac</p> <p>1st August 2020</p> <p>30th October 2021</p> <p>278</p>
--	---	---

Minnie Sharma
Principal

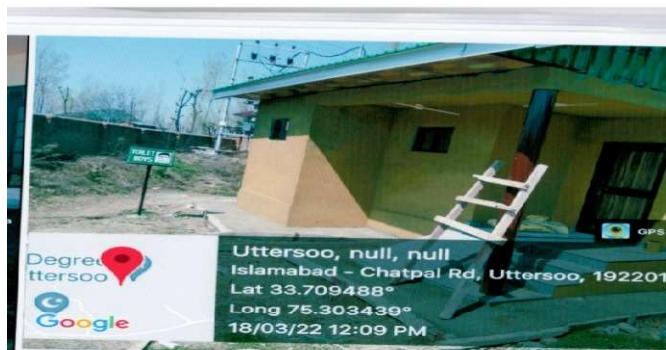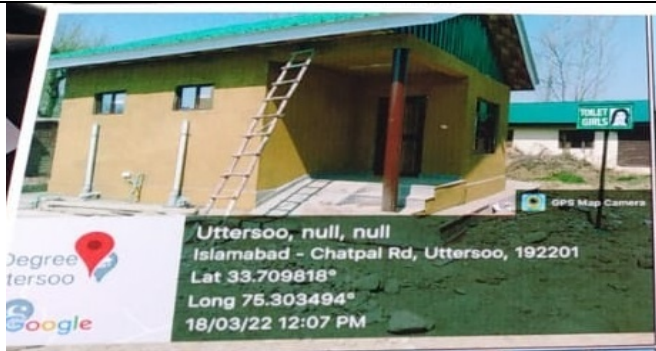


Name of the Work with Location	Construction of Separate Toilet Block
Department/Organization	Higher Education(GDC Uttresoo)
Executive Agency	SICOP
Block/District	Shangus/Anantnag
AA Cost (Rs. In lakhs)	Rs.37.57lacs
Total Cost of Completion/Expenditure incurred ending 3/2022	Rs.35.91 lacs
Date of Start (Month/Year)	2019
No. of Beneficiaries	1113



Name of the Work with Location	Toilet block
Department/Organization	GDC (boys) Kathua
Executive Agency	JKPCC
Block/District	kathua
AA Cost (Rs in Lacs)	71.60
Total cost of Completion/Expenditure incurred ending 3/2022	71.60
Date of Start (M/Y)	09/2019
Date of Completion	03/2022
No of beneficiaries	4500



Name of the work with Location	Construction of Toilet Block, Boundary wall,. pre fabricated class rooms (GDC Marh)
Department/Organization	Higher Education Department
Executive Agency	PWD (R&B)
Block/District	Marh/Jammu
AA Cost (Rs. In lakhs)	124.31
Total Cost of Completion/Expenditure incurred ending 3/2022	93.55
Date of Start (Month/Year)	10-11-2020
Date of Completion (Month/Year)	30-10-2021
No. of beneficiaries	625

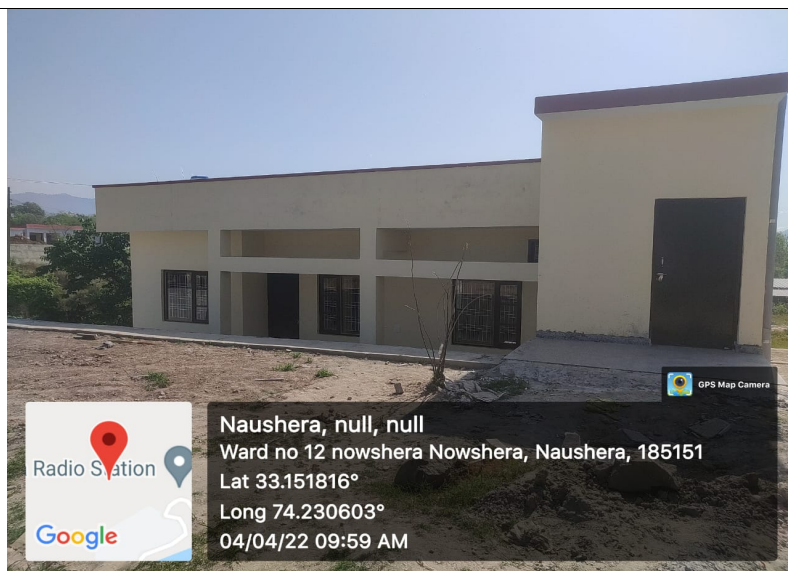


Name of the Work with Location	Construction of Canteen Block at GDC Nowshera
Department/Organization	Higher Education/GDC Nowshera
Executive Agency	PWD
Block/District	Nowshera/Rajouri
AA Cost (Rs in Lacs)	35.60
Total cost of Completion/Expenditure incurred ending 3/2022	32.29
Date of Start (M/Y)	March-2021
Date of Completion	March-2022
No of beneficiaries	1161



Name of the Work with Location	Construction of Virtual Lab at GDC, Pampore
Department/Organization	Higher Education Department
Executive Agency	SICOP/GEM
Block/District	Pulwama
AA Cost (Rs in Lacs)	80.00
Total cost of Completion/Expenditure incurred ending 3/2022	65.00
Date of Start (M/Y)	29/10/2020
Date of Completion	March, 2022
No of beneficiaries	1363




Default
9 February 2022 2:05:03 PM
Lat/Long: 34.0004, 74.933
Altitude: 1407.5
Azimuth: 124.5 deg (Due ESE)



Default
9 February 2022 2:03:44 PM
Lat/Long: 34.0004, 74.931
Altitude: 1400.3
Azimuth: 111.0 deg (E)

Name of the Work with Location	Setting of Chemistry Lab
Department/Organization	Higher Education Department
Executive Agency	GEM
Block/District	Pulwama
AA Cost (Rs in Lacs)	20.00
Total cost of Completion/Expenditure incurred ending 3/2022	20.00
Date of Start (M/Y)	15/10/2021
Date of Completion	March, 2022
No of benefecieries	1363



Plahi, null, null
Unnamed Road, Plahi, 184201
Lat 32.501069°
Long 75.79017°
23/03/22 02:54 PM

Name of the work with location	Browsing Centre
Department/organisation	GDC Basohli
Executive Agency	Non-Construction
Block/District	Basohli/Kathua
AA Cost (Rs. In lakhs)	58.00
Total cost of Completion/Expenditure incurred ending 3/2022	37.13
Date of start(Month/Year)	February/ 2021
Date of Completion (Month/Year)	December/2021
No. of Beneficiaries	35





Automation of Library




Laboratory

Name of the work with Location	Automation of Library /Laboratory GDC Poonch
Department/organization	Higher
Executing Agency	PWD(R&B) Poonch
Block/District	Poonch
AA Cost (Rs. In Lakhs)	30.00
Total Cost of completion /expenditure incurred ending 3/2022	29.98
Date of Start (month/Year)	03/2021
Date of Completion (month/Year)	03/2022
No. Of beneficiaries	1913

	Name of the work with location	Development of Browsing Centre at GDC Women Anantnag
	Department/Organization	Higher Education Department
	Executive Agency	GeM
	Block/District	Anantnag
	AA Cost (Rs. In lakhs)	10 lacs
	Total Cost of Completion/Expenditure incurred ending 03/2022	7.75 lacs
	Date of Start (Month/Year)	2022
	Date of Completion(Month/Year)	Completed (03/2022)
	No. of Beneficiaries	4913

	Name of the Work with Location	Development of Browsing centre, with 60 KV Genset, hot & cold AC at GDC, Jourian)
	Department/Organization	Govt. Degree College Jourian
	Executing Agency	Department
	Block/District	BhalwalBrahmana/Jammu
	Estimated Cost (Rs.in Lakhs)	18.00.lakhs
	Total Expd. incurred ending 03/2022 (Rs. in Lakhs)	12.67 lakhs
	Project initiation year	2021
	Date of Completion	02/2022

	No. of beneficiaries	314
	Name of the work with Location	Skill Centre (GDC Marh)
	Department/Organization	Higher Education Department
	Executive Agency	PWD (R&B)
	Block/District	Marh/Jammu
	AA Cost (Rs. In lakhs)	10
	Total Cost of Completion/Expenditure incurred ending 3/2022	9.9861
	Date of Start (Month/Year)	04-02-2022
	Date of Completion (Month/Year)	10-03-2022
	No. of beneficiaries	625



Name of the work with Location	Construction of Bore Well for underground water in GDC Bani
Department/Organization	Higher Education (GDC Bani)
Executive Agency	Jal Shakti PHE(M) GWD Division Jammu
Block/District	Bani/ Kathua
AA Cost (Rs. in Lakhs)	Rs.15.00 lacs
Total Cost of Completion/Expenditure incurred ending 3/2022	Rs. 14.77 Lacs
Date of Start (Month/Year)	March-2022
Date of Completion (Month/Year)	March-2022
No. of beneficiaries	500 Students





Name of the work with Location: Chain Link	Fencing of Additional Land
Department/Organization	Higher Education Deptt. (GDC Ramban)
Executing Agency	PWD (R&B) Ramban
Block/District	Ramban
AA Cost in Lakhs	53.90 lacs
Total Expdt. Incurred ending 3/2022	53.90 lacs
Project Initiation Year	2019-20
Date of Completion MM/YY	December 2021
No of beneficiaries	730



Name of the work with Location	Construction of Chainlink fencing
Department/organization	Higher Education/GDC Chadoora
Executing Agency	SICOP
Block/District	Chadoora
AA Cost (Rs. In Lakhs)	83.61
Total Cost of completion /expenditure incurred ending 3/2022	83.61
Date of Start (month/Year)	24.02.2021
Date of Completion (month/Year)	20.03.2022
No. Of beneficiaries	171




Name of the work with location	Establishment of GDC Zainapora (renovation of make shift accommodation)
Department/Organization	Higher Education
Executing Agency	R & B
Block/District	Zainapora/ Shopian
AA cost (Rs. In lakhs)	15 Lac
Total cost of completion/expenditure incurred ending 3/2022	12.18 lacs
Date of Start (Month/Year)	March 2020
Date of completion (Month/Year)	August 2021
No. of Beneficiaries	354

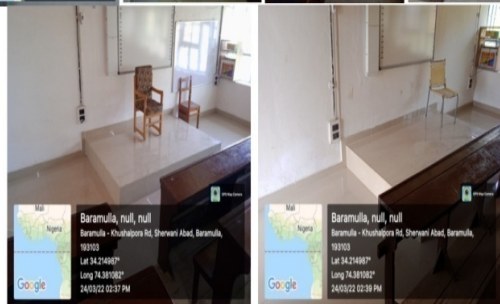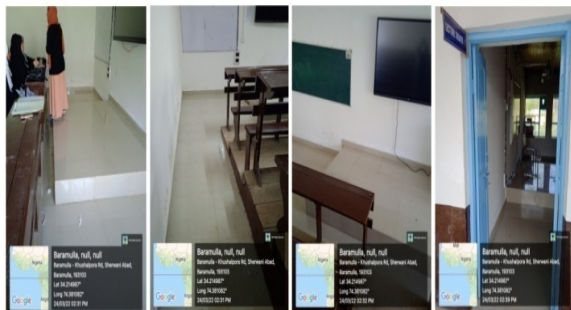

MAIN BUILDING CLASS TILLES - VITRIFIED TILLING

Name of the work with location	1Up gradation of College Buildings by way of damaged plaster, painting, vitrified tiling
Department/Organization	Higher Education Department/ Govt. Degree College Baramulla
Executing Agency	JK SICOP
Block/District	Baramulla/Baramulla
AA Cost (Rs. in lakhs)	69.16 Lakhs
Total cost of Completion/Expenditure incurred ending 03/2022)	Rs. 33.00 Lakhs
Date of Start (Month/Year)	2020-21
Date of Completion (MM/YYY)	December 2021
No. of beneficiaries	4130

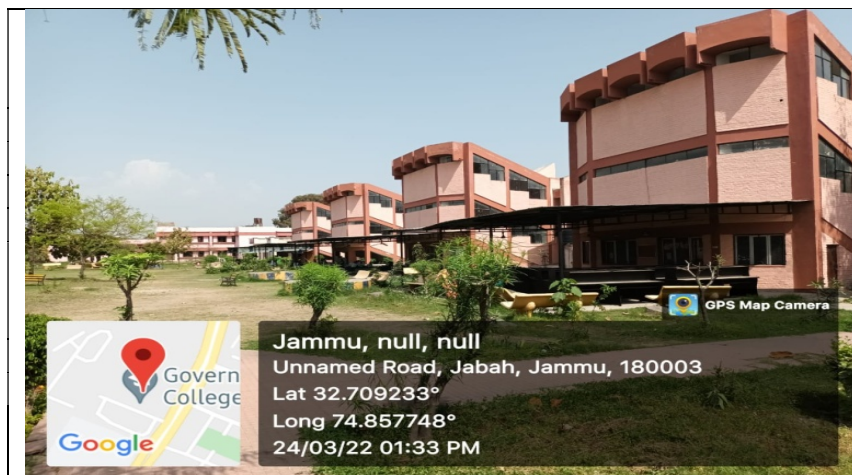


Name of the Work with Location	Improvement and upgradation including water proofing of 7 blocks
Department/Organization	Higher Education/GCW Gandhi Nagar
Executive Agency	PWD
Block/District	Jammu
AA Cost (Rs in Lacs)	121.00 Lacs
Total cost of Completion/Expenditure incurred ending 3/2022	120.64 Lacs
Date of Start (M/Y)	December 2019
Date of Compeltion	10/2021
No of beneficiaries	6000



Name of the Work with Location	Repair and Renovation of Office
Department/Organization	Higher Education/GCW Gandhi Nagar
Executive Agency	PWD
Block/District	Jammu
AA Cost (Rs in Lacs)	20.70 Lacs
Total cost of Completion/Expenditure incurred ending 3/2022	11.60
Date of Start (M/Y)	03/2021
Date of Compeltion	08/2021
No of benefecieries	300




Name of the work with Location	Up-gradation and modernisation of college Buildings(Adm block, Browsing centre)at GCW Baramulla)
Department / Organization	Higher Education/GCW Baramulla
Executive Agency	R&B
Block / District	Baramulla
AA Cost (Rs. in lakhs)	30.00
Total Cost of Completion / Expenditure incurred ending 3/2022	25.06
Date of Start (Month / Year)	01.06.2021
Date of Completion (Month / Year)	28.12.2021
No. of beneficiaries	2800

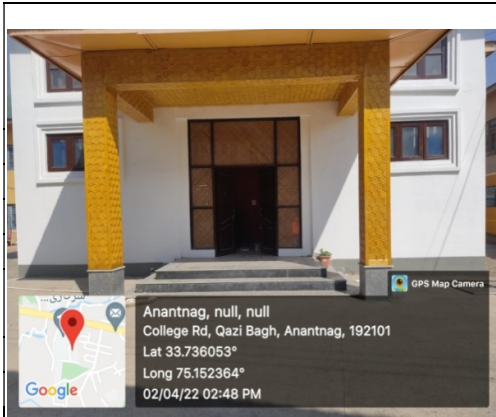


Name of the work with location	Up-gradation of Auditorium at GDC Women Anantnag
Department/Organization	Higher Education Department
Executive Agency	GeM/R&B Division Khanabal
Block/District	Anantnag
AA Cost (Rs. In lakhs)	20 lacs
Total Cost of Completion/Expenditure incurred ending 03/2022	10.82 lacs
Date of Start (Month/Year)	2021
Date of Completion(Month/Year)	Completed (03/2022)
No. of Beneficiaries	4913




Name of the work with Location	Repair/reno. of BCA Block GDC Poonch
Department /organization	Higher Education
Agency	PWD(R&B) Poonch
/District	Poonch
Cost (Rs. In Lakhs)	11.96
Cost of completion /expenditure incurred ending 3/2022	11.61
Date of Start (month/Year)	03/2021
Date of Completion (month/Year)	03/2022
No. of beneficiaries	50

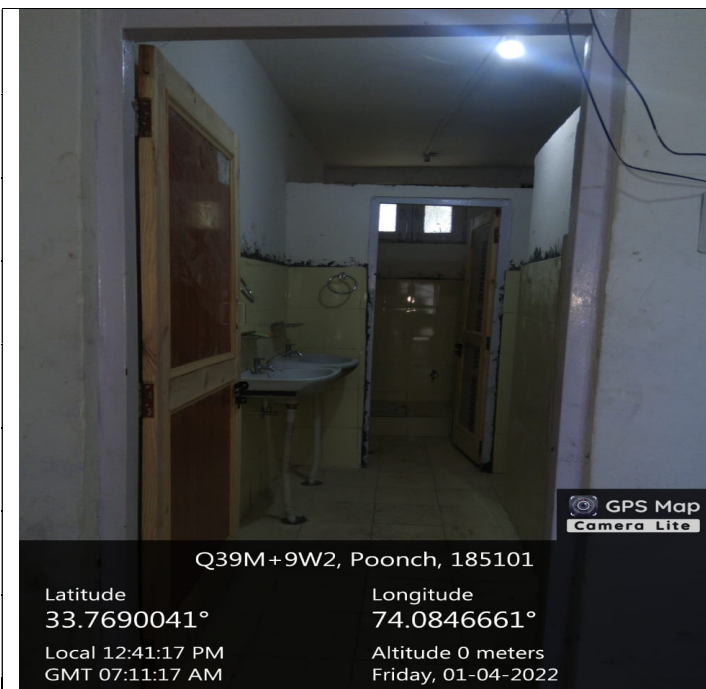


Name of the work with location	Repair of washrooms Girls Hostel, GDC Poonch
Department/Organization	Higher Education
Executing Agency	PWD(R&B) Poonch
Block/District	Poonch
AA Cost (Rs. in lakhs)	12.70
Total cost of Completion/Expenditure incurred ending 03/2022)	12.70
Date of Start (Month/Year)	03/2021
Date of Completion (MM/YYY)	03/2022
No. of beneficiaries	50

 <p>REPAIRING & REARING OF MESH WORK</p>	Name of the work with location	Raising / Repair of mesh wire fencing around GDC Baramulla
	Department/Organization	Higher Education Department/ Govt. Degree College Baramulla
	Executing Agency	JK SICOP
	Block/District	Baramulla/Baramulla
	AA Cost (Rs. in lakhs)	66.70
	Total cost of Completion/Expenditure incurred ending 03/2022)	66.70
	Date of Start (Month/Year)	2020-21
	Date of Completion (MM/YYYY)	February 2022
	No. of beneficiaries	4130

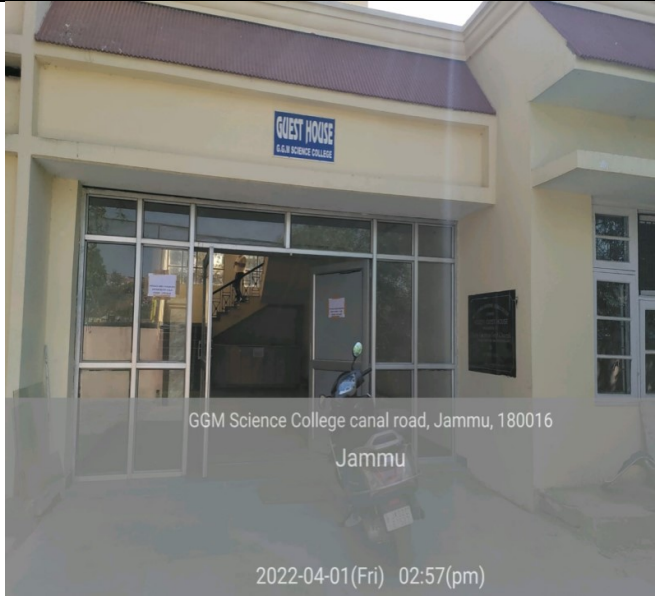
 <p>GGM Science College canal road, Jammu, 180016 Jammu</p> <p>2022-04-01(Fri) 02:57(pm)</p>	Name of the work with Location	Repairing of Guest House at GGM Science College, Jammu
	Department / Organization	Higher Educaxation Department
	Executive Agency	PWD
	Block / District	Jammu
	AA Cost (Rs. in lakhs)	Rs. 33.22 Lacs
	Total Cost of Completion / Expenditure incurred ending 3/2022	Rs. 20.70 Lacs
	Date of Start (Month / Year)	April / 2021
	Date of Completion (Month / Year)	July / 2021
	No. of beneficiaries	3500



Name of the work with location	Const. of paths by way of cement concrete Bed with precast cement concrete tiles along road and Botanical Garden.
Department/Organization	S P COLLEGE
Executive Agency	JK SICOP
Block/District	Srinagar
AA Cost (Rs. In Lakhs)	10.42
Total Cost of Completion/Expenditure incurred ending 03/2023	10.42
Date of start (month /year)	Mar-21
Date of Completion (month /year)	Feb-22
No. of Beneficiaries	3109

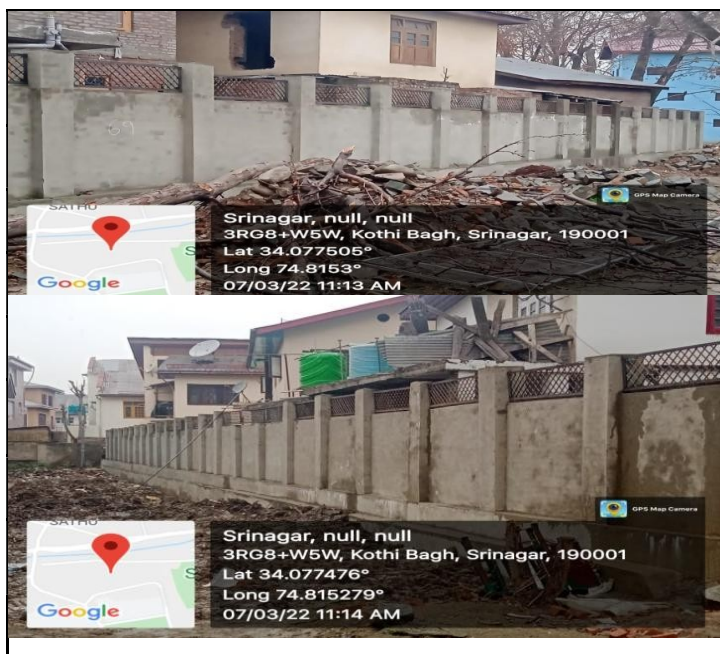

Name of the work with location	Const. of Boundary wall with drain.
Department/Organization	SP COLLEGE
Executive Agency	JKSICOP
Block/District	Srinagar
AA Cost (Rs. In Lakhs)	44.53
Total Cost of Completion/Expenditure incurred ending 03/2024	44.53
Date of start (month/year)	Mar-21
Date of Completion (month/year)	Feb-22
No. of Beneficiaries	3109

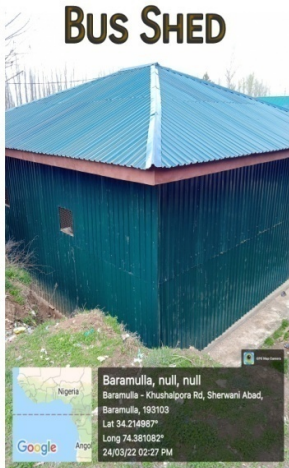


BUS SHED

Name of the work with location	HEDSS2020100543Construction of Bus Shed and store room at GDC Baramulla
Department/Organization	Higher Education Department/ Govt. Degree College Baramulla
Executing Agency	JK SICOP
Block/District	Baramulla/Baramulla
AA Cost (Rs. in lakhs)	18.85 Lakhs
Total cost of Completion/Expenditure incurred ending 03/2022)	Rs. 15.545 Lacs
Date of Start (Month/Year)	2020-21
Date of Completion (MM/YYYY)	January 2022
No. of beneficiaries	4130



Name of the work with Location	Construction of Parking Shed for Students & Staff at GGM Science College, Jammu
Department / Organization	Higher Education Department
Executive Agency	PWD
Block / District	Jammu
AA Cost (Rs. in lakhs)	Rs. 81.67 Lacs
Total Cost of Completion / Expenditure incurred ending 3/2022	Rs. 50.00 Lacs
Date of Start (Month / Year)	May / 2021
Date of Completion (Month / Year)	September / 2021
No. of beneficiaries	3500

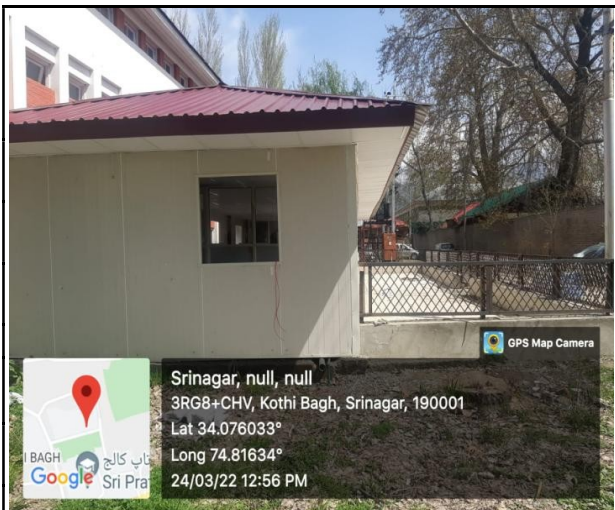

Nameoftheworkwith location	Construction of car parking with steel rooftrusses.
Department/Organization	SPCOLLEGE
ExecutiveAgency	JKSICOP
Block/District	Srinagar
AACost(Rs.InLakhs)	21.91
TotalCostofCompletion/Expenditure incurred ending 03/2022	21.91
Dateofstart(month/year)	Mar-21
DateofCompletion(month/year)	Feb-22
No.ofBeneficiaries	3109



Name of the Work with Location	Construction of Car Parking at GDC, Pampore
Department/Organization	Higher Education Department
Executive Agency	SICOP
Block/District	Pulwama
AA Cost (Rs in Lacs)	34.85
Total cost of Completion/Expenditure incurred ending 3/2022	34.85
Date of Start (M/Y)	25/09/2020
Date of Completion	August , 2021
No of beneficiaries	1363



Name of the work with Location	Platform (GDC Marh)
Department/Organization	Higher Education Department
Executive Agency	PWD (R&B)
Block/District	Marh/Jammu
AA Cost (Rs. In lakhs)	11.54
Total Cost of Completion/Expenditure incurred ending 3/2022	6.67
Date of Start (Month/Year)	20-11-2021
Date of Completion (Month/Year)	15-02-2022
No. of beneficiaries	625



Name of the work with Location	Aluminium partition
	(GDC Marh)
Department/Organization	Higher Education Department
Executive Agency	PWD (R&B)
Block/District	Marh/Jammu
AA Cost (Rs. In lakhs)	5.52
Total Cost of Completion/Expenditure incurred ending 3/2022	3.29
Date of Start (Month/Year)	30-11-2021
Date of Completion (Month/Year)	20-01-2022
No. of beneficiaries	625



Name of the work with Location	63 KVA Sub Station (GDC Marh)
Department/Organization	Higher Education Department
Executive Agency	PWD (R&B)
Block/District	Marh/Jammu
AA Cost (Rs. In lakhs)	7.41
Total Cost of Completion/Expenditure incurred ending 3/2022	7.15
Date of Start (Month/Year)	10-01-2022
Date of Completion (Month/Year)	05-03-2022
No. of beneficiaries	625



Name of the work with Location: Ground Leveling	
	Higher Education Deptt. (GDC Ramban)
Executing Agency	PWD (R&B) Ramban
Block/District	Ramban
AA Cost in Lakhs	21.84lacs
Total Expdt. Incurred ending 3/2022	16.63 lacs
Project Initiation Year	2020-21
Date of Completion MM/YY	December 2021
No of beneficiaries	730



Name of the Work with Location	Construction of Nursing and Medical Institute IUST
Department/Organization	Higher Education Department
Executive Agency	University Engg. Wing
Block/District	Pulwama
AA Cost (Rs in Lacs)	707.61
Total cost of Completion/Expenditure incurred ending 3/2022	707.61
Date of Start (M/Y)	2014-15
Date of Completion	2021-22
No of beneficiaries	





Name of the Work with Location	Construction of Central Library at BGSBU Rajouri
Department/Organization	Higher Education Department
Executive Agency	University Engg. Wing
Block/District	Rajouri
AA Cost (Rs in Lacs)	1091.70
Total cost of Completion/Expenditure incurred ending 3/2022	1091.70
Date of Start (M/Y)	2016
Date of Completion	2021-22
No of beneficiaries	



Name of the Work with Location	Construction of Botany and Zoology Block at BGSU Rajouri
Department/Organization	Higher Education Department
Executive Agency	University Engg. Wing
Block/District	Rajouri
AA Cost (Rs in Lacs)	687.00
Total cost of Completion/Expenditure incurred ending 3/2022	687.00
Date of Start (M/Y)	2016-17
Date of Completion	2021-22
No of beneficiaries	



Name of the Work with Location	School of Paramedical college South Campus Kashmir University
Department/Organization	Higher Education Department
Executive Agency	University Engg. Wing
Block/District	Srinagar
AA Cost (Rs in Lacs)	1050.00
Total cost of Completion/Expenditure incurred ending 3/2022	1050.00
Date of Start (M/Y)	2016-17
Date of Completion	2021-22
No of beneficiaries	

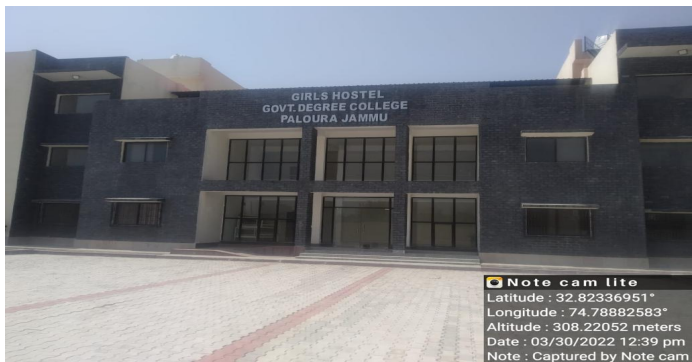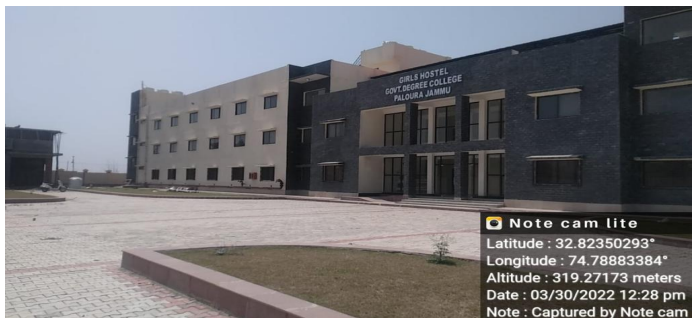

Name of the works with location

**Construction of Girls Hostel
Govt. Degree College GDC
Paloura**

Department/organization

**Higher Education/GDC
Paloua**

Executing Agency

J&K housing Board

Block/District

Jammu

AA Cost (Rs in lakhs)

1250.00

**Total Cost of completion
/Expenditure incurred ending
3/2022**

1125.00

Date of Start (Month Year)

11/2017

**Date of completion
(Month/Year)**


10/2021

No of beneficiaries


300



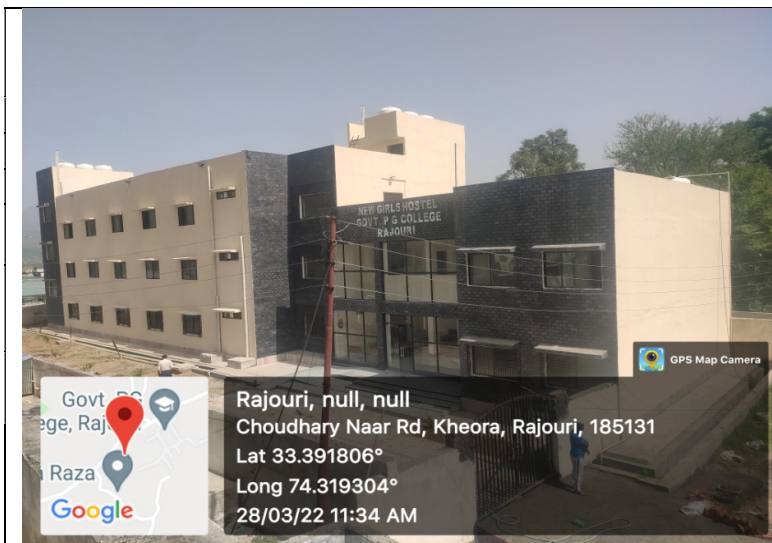

Name of the works with location	Construction of Girls Hostel Govt. Degree College Bhaderwah
Department/organization	Higher Education
Executing Agency	Police Housing Corporation J&K
Block/District	Bhaderwah/Doda
AA Cost (Rs in lakhs)	465.00
Total Cost of completion /Expenditure incurred ending 3/2022	450.00
Date of Start (Month Year)	11/2018
Date of completion (Month/Year)	12/2021
No of beneficiaries	80





Name of the Work with Location	Construction of Girls Hostel under PMDP (GDC Rajouri)
Department/Organization	Higher Education (GDC Rajouri)
Executive Agency	HB J&K
Block/District	Rajouri
AA Cost (Rs. In lakhs)	Rs. 500 Lakhs
Total Cost of Completion/Expenditure incurred ending 3/2022	Rs. 455.86 Lakhs
Date of Start (Month/Year)	17-05-2018
No. of Beneficiaries	124 Students Per Session


 <p>Latitude: 33.767802 Longitude: 74.093918 Elevation: 988.06±1 m Accuracy: 68.4 m Time: 01-07-2022 12:17 Note: GDC Poonch girls toilet block</p> <p>Estimated Cost: 12.31 Lacs Powered by NoteCam</p>	Name of the work with location	Construction of Girls Toilet Block GDC Poonch
	Department/Organization	HED
	Executing Agency	PWD (R&B)
	AA Cost (Rs. In Lakhs)	12.31
	Total Cost of Completion/Expenditure incurred ending 03/2022	12.31
	Date of start (month/year)	Mar-2021
	No. of Beneficiaries	980

 <p>Latitude: 33.767122 Longitude: 74.093457 Elevation: 984.37±1 m Accuracy: 15.8 m Time: 01-07-2022 12:35 Note: GDC Poonch canteen cafeeteria</p> <p>Powered by NoteCam</p>	Name of the work with location	Upgradation of Canteen/Cafeteria Block GDC Poonch
	Department/Organization	HED
	Executing Agency	PWD (R&B)
	AA Cost (Rs. In Lakhs)	3.58
	Total Cost of Completion/Expenditure incurred ending 03/2022	3.58
	Date of start (month/year)	Mar-2021
	No. of Beneficiaries	1913

	Name of the work with location	Repair/Renovation of Existing Auditorium GDC Poonch
	Department/Organization	HED
	Executing Agency	PWD (R&B)
	AA Cost (Rs. In Lakhs)	3.58
	Total Cost of Completion/Expenditure incurred ending 03/2022	3.58
	Date of start (month/year)	Mar-2021
	No. of Beneficiaries	1913

	Name of the work with location	Construction of Common Room for students GDC Poonch
	Department/Organization	HED
	Executing Agency	PWD (R&B)
	AA Cost (Rs. In Lakhs)	43.28
	Total Cost of Completion/Expenditure incurred ending 03/2022	43.28
	Date of start (month/year)	Mar-2021
	No. of Beneficiaries	1913

	Name of the work with location	Repair /Renovation upgradation of Classrom GDC Poonch
	Department/Organization	HED
	Executing Agency	PWD (R&B)
	AA Cost (Rs. In Lakhs)	7.98
	Total Cost of Completion/Expenditure incurred ending 03/2022	7.98
	Date of start (month/year)	Mar-2021
	No. of Beneficiaries	100


	Name of the work with location	Construction of Canteen Block at GDC Sunderbani
	Department/Organization	
	Executing Agency	PWD (R&B)
	AA Cost (Rs. In Lakhs)	23.25
	Total Cost of Completion/Expenditure incurred ending 03/2022	23.25
	Date of start (month/year)	Mar-2021
	No. of Beneficiaries	913





Name of the work with location	Construction of Toilet Block at GDC Sunderbani
Department/Organization	
Executing Agency	PWD (R&B)
AA Cost (Rs. In Lakhs)	44.65
Total Cost of Completion/Expenditure incurred ending 03/2022	44.65
Date of start (month/year)	Dec-2020
No. of Beneficiaries	913





Name of the work with location	Common Room Facility for StudentsGDC Rajouri
Department/Organization	HED
Executing Agency	PWD (R&B)
AA Cost (Rs. In Lakhs)	79.60
Total Cost of Completion/Expenditure incurred ending 03/2022	45.00
Date of start (month/year)	Dec -2020
No. of Beneficiaries	2500

	Name of the work with location	Repair Renovation/Addition & Alteration of staff Room & office GCW Udhampur
	Department/Organization	HED
	Executing Agency	PWD (R&B)
	AA Cost (Rs. In Lakhs)	59.50
	Total Cost of Completion/Expenditure incurred ending 03/2022	44.00
	Date of start (month/year)	Jun-2020
	No. of Beneficiaries	100


	Name of the work with location	Construction of girls common room GCW Udhampur
	Department/Organization	
	Executing Agency	PWD (R&B)
	AA Cost (Rs. In Lakhs)	99.00
	Total Cost of Completion/Expenditure incurred ending 03/2022	36.00
	Date of start (month/year)	Mar-2021
	No. of Beneficiaries	2950

	Name of the work with location	Construction of Toilet Block GDC Larnoo
	Department/Organization	HED
	Executing Agency	PWD (R&B)
	AA Cost (Rs. In Lakhs)	43.88
	Total Cost of Completion/Expenditure incurred ending 03/2022	41.40
	Date of start (month/year)	Nov-2020
	No. of Beneficiaries	

	Name of the work with location	Construction of Toilet Block male/ Female GDC Kupwara
	Department/Organization	HED
	Executing Agency	JKPCC
	AA Cost (Rs. In Lakhs)	44.65
	Total Cost of Completion/Expenditure incurred ending 03/2022	44.65
	Date of start (month/year)	Jun -2018
	No. of Beneficiaries	540

 <p>KUPwara sulkoot, 193222</p> <p>Latitude 34.53699168283492° Longitude 74.25512194633484°</p> <p>Local 11:17:51 AM Altitude 1610 meters</p> <p>GMT 05:47:51 AM Monday, 04-04-2022</p>	Name of the work with location	Construction of Canteen Block GDC Kupwara
	Department/Organization	HED
	Executing Agency	JKPCC
	AA Cost (Rs. In Lakhs)	23.25
	Total Cost of Completion/Expenditure incurred ending 03/2022	23.25
	Date of start (month/year)	Jun -2018
	No. of Beneficiaries	540

Automation of Toilet Block GDC Larnoo

 <p>Udhampur</p> <p>Google</p> <p>null, null, null Unnamed Road, Leray, 182101 Lat 32.926731° Long 75.125258° 04/04/22 02:05 PM</p>	Name of the work with location	Construction of Additional Classroom/Labs on first floor of existing Chemistry block and toilet GDC Udhampur
	Department/Organization	HED
	Executing Agency	University works department
	AA Cost (Rs. In Lakhs)	99.50
	Total Cost of Completion/Expenditure incurred ending 03/2022	60.25
	Date of start (month/year)	Jul-2019
	No. of Beneficiaries	700



Extension/Modernization of Administrative Building
Jammu University

Name of the work with location	Extension/Modernization of Administrative Building Jammu University
Department/Organization	HED
Executing Agency	University works department
AA Cost (Rs. In Lakhs)	120.00
Total Cost of Completion/Expenditure incurred ending 03/2022	120.00
Date of start (month/year)	Jun -2019
No. of Beneficiaries	130

Construction of canteen complex in the GCW Udhampur

Year of initiation: 2019

Year of Completion: Dec 2021

Completion Cost: 48.29 lacs

Scheme: Local fund

Beneficiary: 3000



